



Final steps and discussion

Elsa Batista

Portuguese Institute for Quality

Final Workshop MeDDII

2022-11-24

Final points

- ✓ Update Webpage and Zenodo with new reports and deliverables
- ✓ Conclude D7 and D8 of WP4
- ✓ Conclude D9 of WP5
- ✓ Make final reporting, D10
 - ✓ Final technical report
 - ✓ Impact report
 - ✓ Exploitation plan
 - ✓ Publishable summary
 - ✓ Data management plan
 - ✓ Horizon 2020 questionnaire
 - ✓ Financial report
- ✓ Final newsletter

General problems

- Covid 19 and delay in measurements, need 6 month extensions and maybe it was not enough
- Getting loaned equipment from manufactures for tests
- The pain pump was broken during the tests of WP3
- Difficulty in getting the medical liquid/drugs for tests
- Problems with harmonization of definitions VIM/medical terminology e.g error
- Difficulty in contact regulators, EC
- Difficulty in contact medical associations, only ESICM available



Lessons learned

- Improve communication with end users - tell a more “sexy” story
- More interactions with advisory board and stakeholders
- More focus on medical problems, bottom up, not top down
- Understand the importance of metrology in the medical world, what is relevant to calibrate or not and in what conditions of use
- Better dissemination tools, more onsite training
- Need for a equilibrium between metrological assessment, good practice of use and identification of critical devices
- Understand better the role of metrology in the clinical world



Future

- Proposal of PRT for normative call in 2023, start in January 2023
- Update e-learning course
- EURAMET projects need high level science and new developments in metrology





Participant details:

a. Partners (participants who will accede to the Grant Agreement)

no.	Participant Type	Short Name	Organisation legal full name	Country
1	Internal Funded Partner	IPQ	Instituto Português da Qualidade, I.P.	Portugal
2	Internal Funded Partner	CETIAT	Centre Technique des Industries Aérauliques et Thermiques	France
3	Internal Funded Partner	CMI	Cesky Metrologicky Institut	Czech Republic
4	Internal Funded Partner	DTI	Teknologisk Institut	Denmark
5	Internal Funded Partner	METAS	Eidgenössisches Institut für Metrologie METAS	Switzerland
6	Internal Funded Partner	NEL	TUV SUD Limited	United Kingdom
7	Internal Funded Partner	NQIS*	National Quality Infrastructure System	Greece
8	Internal Funded Partner	RISE	RISE Research Institutes of Sweden AB	Sweden
9	External Funded Partner	DNV	DNV Netherlands B.V.	Netherlands
10	External Funded Partner	HSG-MIT	Hahn-Schickard-Gesellschaft für angewandte Forschung e.V.	Germany
11	External Funded Partner	INESC MN	INESC Microsistemas e Nanotecnologias-Instituto de Engenharia de Sistemas de Computadores Para os Microsistemas e as Nanotecnologias	Portugal
12	External Funded Partner	THL	Technische Hochschule Lübeck	Germany
13	External Funded Partner	UMCU	Universitair Medisch Centrum Utrecht	Netherlands
14	External Funded Partner	STRATH	University of Strathclyde	United Kingdom
15	Unfunded Partner	BHT	Bronkhorst High-Tech BV	Netherlands
16	Unfunded Partner	KRISS	Korea Research Institute of Standards and Science	Republic of Korea

Thank you to the MeDDII Team!!!!

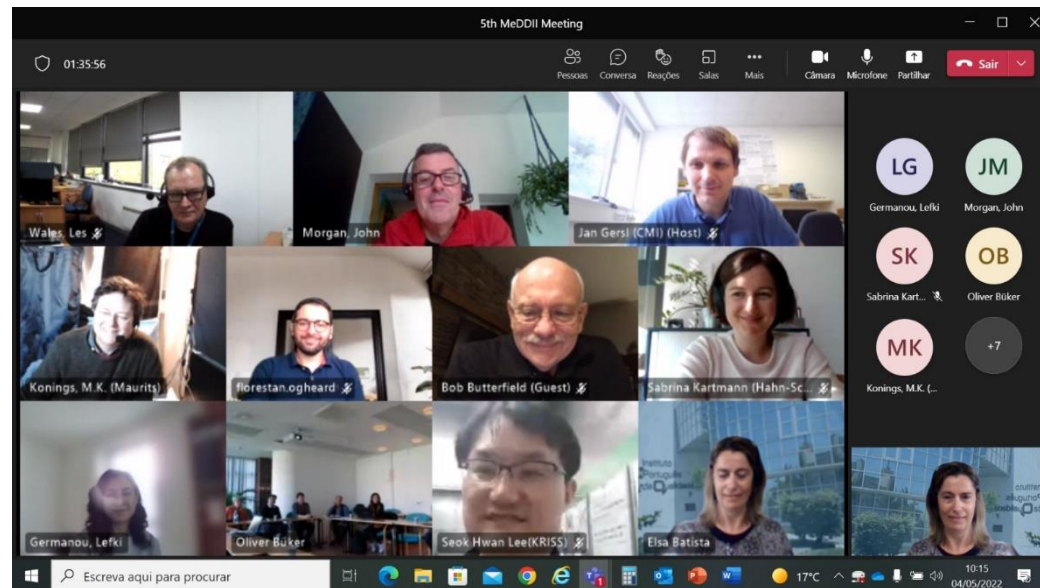



THANK YOU



Elsa Batista

ebatista@ipq.pt

+351212948167
